



Project Plan

A Labor Day Half Marathon for Warangal

05/31/2023

TABLE OF CONTENTS

Project Charter And Scope	3
Work Break-Down Structure	13
Project Schedule	15
Project Budget	22
Empathy Map	26
Project Closure	27
List of Sponsors	35

PROJECT CHARTER AND SCOPE

1. Business Need/Project Objectives:

The goal of this project is to design and execute a successful Labor Day Half Marathon event in Warangal, Telangana, India that promotes community participation, physical health, and local humanitarian causes. The event seeks to provide a memorable experience for participants while promoting Warangal's unique traits and natural beauty by bringing together runners of all abilities and cultivating an inclusive environment. The project strives to establish the Labor Day Half Marathon as an annual event that contributes to the well-being and vibrancy of the community via excellent planning, promotion, and engagement with local stakeholders.

Project Scope

The major goal of the project is to promote fitness and a healthy lifestyle, to increase community engagement, to increase understanding of Warangal's cultural legacy, and to offer participants with an amazing experience. A well-organized event schedule, planned marathon routes, communication channels, a marketing campaign, and event-day activities are among the deliverables. The scope constraints state that just the half-day marathon event will be covered, with no extra activities or infrastructure changes. Volunteers, appropriate funding, and the necessary approvals are all assumed. The event will be finished in a half-day by obeying all local laws, and there will be constraints due to limited resources. Project managers, event committees, participants, sponsors, government officials, volunteers, and spectators are all examples of stakeholders.

Being the project manager, it is my duty to encourage timely and thorough deliveries to the customer because certain activities of this project must be finished before another work can begin and other tasks have to be accomplished concurrently. Since I am the only one working on this project, I clearly understand which job should be completed first and which should come after, as well as how to use the available physical and human resources to complete the tasks.

The project is expected to take 5 months, from January 2023 to May 31, 2023. The Marathon is scheduled for May 31st, 2023. The date for this project cannot be adjusted since the essential approvals have been obtained and the plan needs to be changed correspondingly, which is extremely hard. The total budget for the project is \$22,800 (19 lakh INR). This budget number clearly contains all of the expenditures stated in this project, and the budget is not exceeded until and until an issue emerges during the implementation phase.

3. Project Requirements:

- Route Planning
- Permits and Logistics
- Volunteer Management
- Participant Registration
- Marketing and Promotion
- Safety and Medical Support

4. Product Description/Deliverables:

- Event Plan
- Half Marathon Route

- Participant Management System
- Volunteer Coordination Plan
- Volunteer Coordination Plan

5. Stakeholders

- Project Manager: Oversees project planning, coordination, and implementation.
- Event Committee: A group of people who are in charge of certain aspects of the event, such as logistics, marketing, participant registration, and volunteer coordination.
- Participants: Individuals who sign up to run the marathon.
- Sponsors: Organizations that contribute financially or in-kind to the event.
- Local Authorities: Relevant government departments and organizations in charge of issuing licenses and enforcing rules.
- Volunteers: People who provide their time and talents to help with event planning and administration.
- Spectators: People who come to the event to cheer on the competitors and enjoy the festivities.

6. Affected business operations or systems:

Given that Warangal is not a major metropolis, organizing a half-day marathon event can have a variety of implications for corporate operations or systems. The following are some possible regions that can be affected:

- **Transportation and Traffic Management:** The marathon event may result in temporary road closures or detours, potentially causing delays in transportation and impacting businesses that rely on smooth traffic flow.
- **Local Businesses:** Nearby hotels, restaurants, and retail establishments may experience increased customer traffic as participants and spectators visit the area. However, they may also face challenges related to crowd management, increased demand, or competition during the event.
- **Safety and Security:** Additional security measures and personnel may be required to ensure the safety of participants and spectators. Businesses located near the event venue may need to comply with security protocols or access restrictions.
- **Marketing and Advertising:** The marathon event provides opportunities for businesses to increase their brand visibility and reach a diverse audience. Sponsoring the event or placing advertisements in event materials can be effective marketing strategies.
- **Employee Participation and Morale:** Encouraging employee participation in the marathon can promote team building, health and wellness initiatives, and boost employee morale. Businesses can consider supporting their employees' participation through incentives or flexible work schedules.

7. Implementation Plan:

The implementation plan for the half-day marathon event in Warangal involves defining event objectives, forming an event committee, determining the budget and funding sources, obtaining necessary permits and permissions, developing an event plan encompassing logistics,

participant registration, routes, and entertainment, promoting the event through various channels, coordinating volunteers and event logistics, ensuring safety and security, executing the event with participant check-in, route management, aid stations, and ceremonies, monitoring and evaluating the event, and concluding with post-event activities. Flexibility and adaptability are crucial throughout the process to ensure a successful and enjoyable event.

Primary Clients:

This event is organized by the Greater Warangal Municipal Corporation of India. It is a responsible body that completely takes care of police permissions and traffic management along the route. This entire plan will be brought to the notice of the local member of the legislative assembly (MLA) of Warangal.

GWMC has a tie-up with the Good Future Personality Development Services Society which is involved in the making of a website to book the registrations for the participants and audience. I am the person who is managing this organization to get all the necessary things done according to the plan and simultaneously get in coordination with the GWMC.

There are a few people from GWMC as part of the organizing committee who takes care of event management, logistics, marketing, and community engagement. Each committee member will be assigned specific roles and responsibilities to ensure smooth coordination. We have a talk with two colleges about providing the students as volunteers for this event.

For sponsorship and funding, we are creating a gateway in the website which is developed by Good Future Personality Development Services Society. I will personally develop a comprehensive publicity plan to generate buzz and media coverage. We are committed to environmental sustainability. Therefore, we will implement waste management and recycling

measures throughout the event. I will encourage participants and volunteers to minimize waste and promote eco-friendly practices. I will ensure that our event is not just a marathon but an experience to remember. We will plan for entertainment activities and engaging elements along the route to boost participant morale and create an enjoyable atmosphere. From live music to cheering squads, and motivational signboards to interactive experiences, we will make sure that everyone has a fantastic time. I will collaborate with medical professionals to establish a robust medical support plan. Our volunteers will arrange for medical stations along the route and provide ample medical personnel, ambulances, and first-aid kits. We will communicate safety guidelines to participants and spectators, including heat safety precautions and COVID-19 protocols. I will personally arrange for necessary logistics, including timing systems, start and finish line structures, water stations, medical aid, and transportation facilities. I will ensure that all equipment is properly tested and prepared before the event day.

8. Project Does Not Include:

- Individual Participant Training
- Travel and Accommodation Arrangements
- Personal Equipment and Gear
- Personal Medical and Health Services
- Post-Event Travel or Excursions

9. Pre-assigned Resources:

- Human Resources
- Physical Resources


- Financial Resources
- Partnerships and Sponsorships
- Communication Channels

10. High-Level Timeline/Schedule

January	✓ Define event objectives and establish the event committee. ✓ Begin preliminary budget planning and identify potential funding sources. ✓ Initiate discussions with local authorities regarding permits and permissions.
February	✓ Finalize the event budget and secure funding sources. ✓ Obtain necessary permits and permissions for the event. ✓ Develop the event plan, including logistics, participant registration, and marketing strategies.
March	✓ Launch the event marketing and promotion campaign. ✓ Open participant registration and start collecting fees (if applicable). ✓ Continue refining the event plan and coordinating with vendors and suppliers.
April	✓ Intensify marketing efforts to attract participants and sponsors. ✓ Coordinate volunteer recruitment and training. ✓ Finalize event logistics, including infrastructure, security measures, and medical aid stations.
May	✓ Conduct participant registration and finalize participant lists. ✓ Conduct a comprehensive review of event preparations. ✓ Execute the half-day marathon event, ensuring smooth operations and participant safety. ✓ Conduct post-event evaluations, gather feedback, and wrap up any remaining tasks or financial settlements.

11. Route Map:

Embark on a breathtaking journey through the heart of Warangal, where the spirit of athleticism intertwines with the city's glorious heritage. The half-day marathon commences at the iconic National Institute of Technology Warangal, an emblem of knowledge and innovation. As participants lace up their running shoes, they traverse the vibrant streets, guided by the trail's scenic tapestry. The route meanders through the awe-inspiring Kakatiya Zoo Park, where the harmonious symphony of nature reverberates through every step. Runners then find themselves embraced by the verdant splendor of the Warangal Biodiversity Junction, where the rich flora and fauna create a sanctuary of serenity. The journey continues to unfold as the marathoners enter the hallowed grounds of Police Grounds, a symbol of strength and unity. Finally, as the finish line draws near, the captivating Wadepally Lake Viewpoint 3 emerges, inviting weary feet to rest and eyes to behold the captivating vista. Covering a total distance of 20.5 kilometers (13.1 miles), this exhilarating marathon promises an unforgettable experience, encapsulating the essence of Warangal's majestic beauty and indomitable spirit.

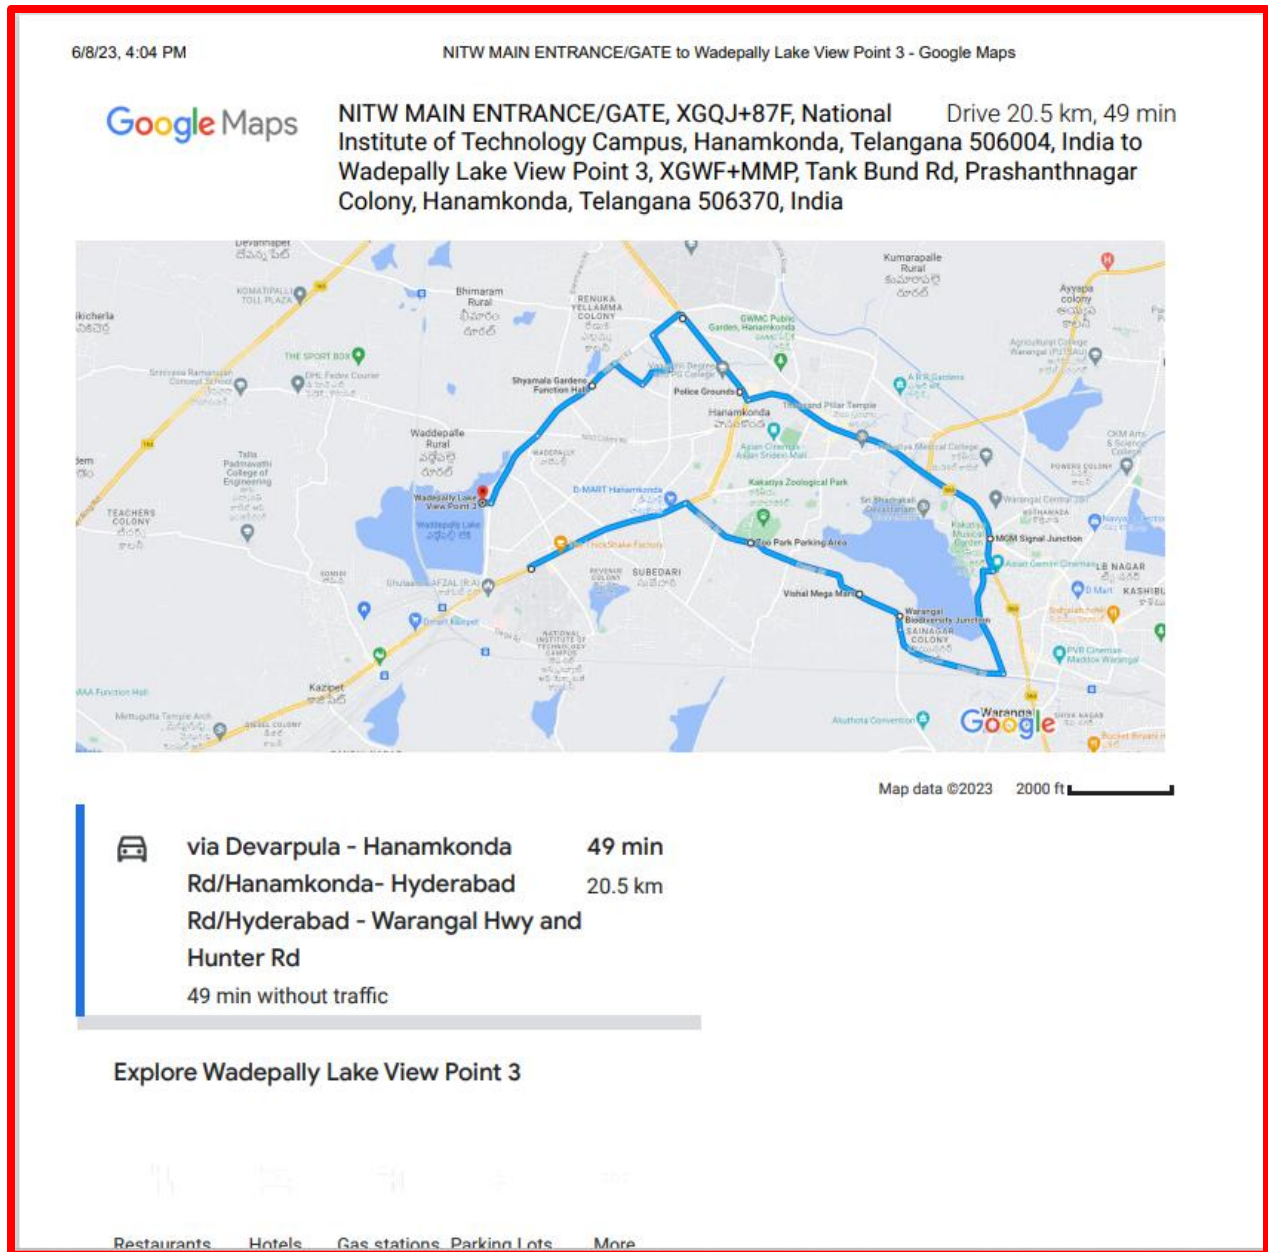

The race has to start very early (at 6 am) as the temperature in the month of May is really hot. This is to take advantage of the cooler temperatures in the morning. This helps minimize exposure to intense sunlight and heat during the peak hours of the day.

12. Approval and Authority to Proceed:

The product is fully functioning, tested and verified. It is ready to go to the market.

NAME	TITLE	DATE


Approved by

Date

Approved by

Date

WORK BREAKDOWN STRUCTURE

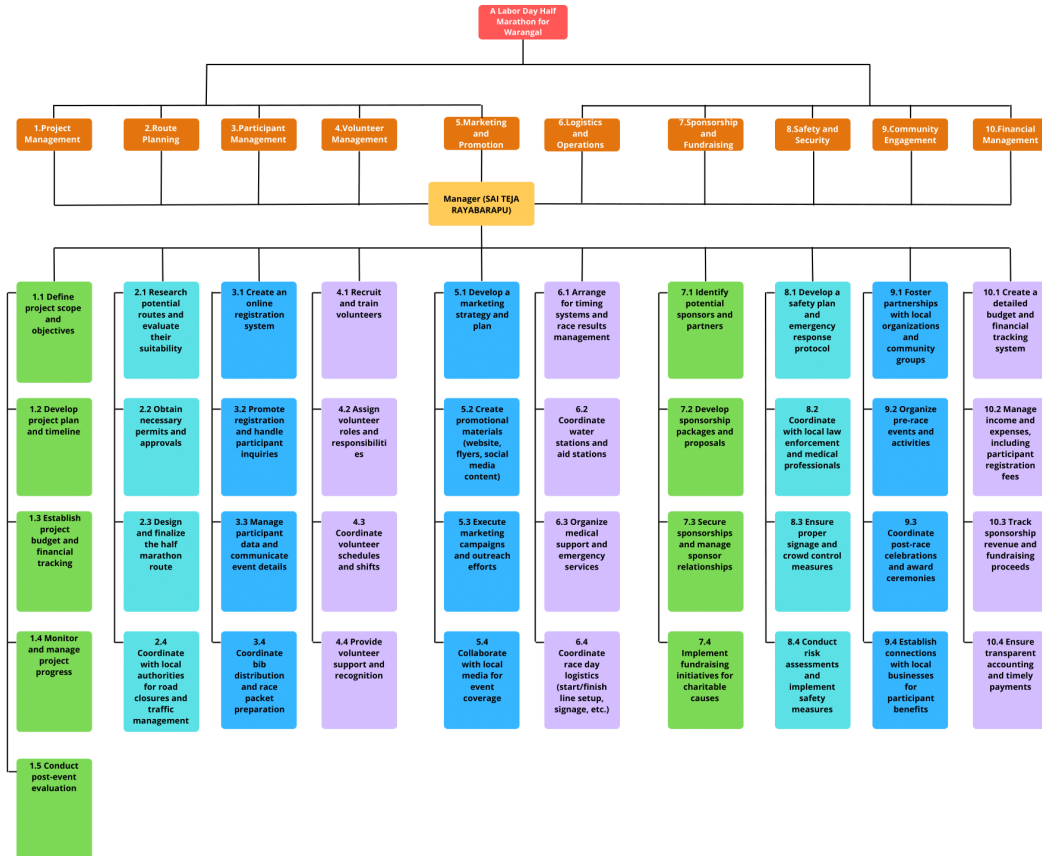


The above structure summarizes all the deliverables and tasks to be performed throughout this event. This is mainly divided into four steps:

1. The Title
2. The Ten Main Deliverables
3. Project Manager Responsible for every action
4. The sub-deliverables

All the events which are part of this project are categorized into ten main sections which are arranged in ascending order. As I am the only person responsible for completing this project, I have a

clear idea about which event to occur first and which one to come next. I did not make the structure into pre, present and post but I did cover all the events in the exact order of which they occur as a part of sub-deliverables. The main ten sections are named after the activities which they include throughout the project's execution.

Work Breakdown Structure 2

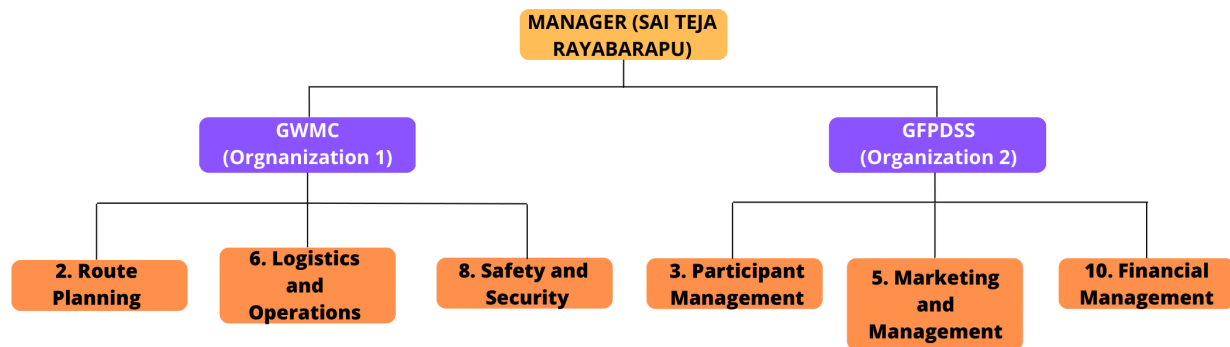

The second structure clearly describes the points discussed in the scope of the project, which includes two main client organizations. So these two organizations are responsible to deliver the major amount of sub-deliverables across six different sections mention in the first structure. The manager (SAI TEJA RAYABARAPU) is responsible to maintain the coordination between the two organizations and ensure everything is going according to the plan.

PROJECT SCHEDULE

S N O	Activity List	Activity Duration List	Time Taken (Days)	Activity Resource List	Definition, Attribute, Milestone
1	Define project scope and objectives. - Review project requirements and stakeholder expectations. - Conduct initial meetings with key stakeholders to gather input. - Clearly define the scope and objectives in a project scope document.	JAN 1 TO JAN 31	10	1. Human Resources: - Sai Teja (Project Manager) - GWMC Officials - GFPDSS Officials - Volunteers 2. Equipment and Tools: - Computer/laptop - Project management software - Communication tools (email, messaging platforms) - Collaboration tools (project management platforms, shared document repositories)	➤ Definition: Clearly define the scope and objectives of the project. ➤ Attribute: Scope document created. ➤ Milestone: Completion of the project scope document with all things ticked as per the activity list.
2	Conduct initial research on potential routes. - Gather information on possible routes for the half marathon. - Evaluate the suitability of each route based on distance, terrain, and safety. - Analyze factors such as road closures, permits, and community impact for each potential route.		7	3. Facilities: - Personal workspace 4. Materials and Supplies: - Office supplies (paper, pens, folders) - Software licenses	➤ Definition: Research and evaluate potential routes for the half marathon event. ➤ Attribute: Route options identified without any obstacles. ➤ Milestone: Completion of initial route research with a proper track path.
3	Begin developing the project plan and timeline. - Identify project tasks and activities. - Determine the dependencies and sequence of activities. - Create a preliminary timeline and allocate resources to each task.		5	5. Financial Resources: - Project budget - Funding or investment (if applicable) 6. Information and Documentation: - Project plans - Requirements documents - Design documents - User manuals - Reports and templates	➤ Definition: Start creating a detailed project plan and timeline for the event so that everything goes according to the anticipated time. ➤ Attribute: Project plan and timeline draft created. ➤ Milestone: Completion of the initial project plan and timeline.
4	Start volunteer recruitment efforts. - Develop a volunteer recruitment plan. - Advertise volunteer		9	7. External Resources:	➤ Definition: Begin the process of recruiting volunteers for the event. ➤ Attribute: Volunteer recruitment campaign initiated.


	opportunities through various channels. • Screen and interview potential volunteers. • Assign volunteers to specific roles or teams.			• None (I am the only person involved) 8. Time and Schedule: • Project schedule or timeline • Task management software or tools	➤ Milestone: Recruitment of a certain number of volunteers.
5	Finalize project plan and obtain necessary approvals. • Incorporate feedback from stakeholders into the project plan. • Review and revise the timeline based on input from relevant parties. • Obtain necessary approvals from project sponsors or management.	FEB 1 TO FEB 28	6	9. Training and Development: • Training materials or resources for self-improvement (if applicable) 10. Communication and Stakeholder Engagement: • Communication plans (outlining how I will communicate with stakeholders)	➤ Definition: Review and finalize the project plan, considering feedback and obtaining necessary approvals. ➤ Attribute: Approved project plan and timeline. ➤ Milestone: Approval of the project plan.
6	Complete route selection and obtain permits. • Evaluate the research on potential routes and select the most suitable one. • Gather the required documentation and submit permit applications to the appropriate authorities. • Follow up with the authorities to ensure timely approval of permits.		12		➤ Definition: Finalize the selection of the route and acquire the required permits for the event. ➤ Attribute: Route confirmed, and permits obtained. ➤ Milestone: Receipt of all necessary permits.
7	Launch participant registration system and marketing campaigns. • Set up an online registration system to capture participant information. • Develop a marketing plan and create promotional materials. • Launch marketing campaigns through various channels, such as social media, websites, and local advertising.		7		➤ Definition: Set up the registration system for participants and start marketing campaigns to attract participants. ➤ Attribute: Registration system live and marketing campaigns initiated. ➤ Milestone: Opening of participant registration.

8	Continue volunteer recruitment and training. • Advertise ongoing volunteer opportunities and encourage community engagement. • Conduct volunteer training sessions to ensure they understand their roles and responsibilities. • Provide volunteers with necessary resources and materials.	MARCH 1 TO MARCH 31	3		➤ Definition: Replace new volunteers if there are any droppings from the old people and continue to train them on all aspects. ➤ Attribute: Ongoing volunteer recruitment and training efforts. ➤ Milestone: Completion of volunteer training.
9	Execute marketing and promotion strategies. • Implement the marketing plan by executing planned activities. • Coordinate media coverage and press releases. • Monitor the effectiveness of marketing efforts and make adjustments as needed.		9		➤ Definition: Implement marketing and promotion strategies to raise awareness about the event. ➤ Attribute: Marketing and promotion activities ongoing. ➤ Milestone: Achieve a certain level of media coverage.
10	Coordinate with local authorities for road closures and traffic management. • Identify the roads that need to be closed during the event. • Engage with local authorities to obtain necessary permissions and permits for road closures. • Develop a traffic management plan in collaboration with relevant stakeholders.		10		➤ Definition: Collaborate with local authorities to plan road closures and manage traffic during the event. ➤ Attribute: Road closure plan and traffic management strategy developed. ➤ Milestone: Approval of road closure plan.
11	Continue participant registration and communication. • Regularly update the registration system with new participant information. • Communicate event updates and important		5		➤ Definition: Maintain participant registration and keep participants informed about the event updates. ➤ Attribute: Ongoing participant registration and communication. ➤ Milestone: Reaching a certain number of registered participants.

	information to registered participants. • Address participant inquiries and provide assistance as needed.				
12	Finalize sponsorships and fundraising initiatives. • Identify potential sponsors and develop sponsorship packages. • Reach out to potential sponsors and negotiate agreements. • Implement fundraising initiatives, such as crowdfunding campaigns or sponsorship drives.		7		➤ Definition: Secure sponsorships for the event and finalize fundraising initiatives. ➤ Attribute: Confirmed sponsorships and fundraising strategies. ➤ Milestone: Achievement of fundraising target.
13	Intensify marketing efforts and participant engagement. • Increase advertising and promotional activities to attract more participants. • Enhance participant engagement through social media campaigns, contests, or interactive activities. • Collaborate with local organizations or influencers to expand reach and engagement.	APRIL 1 TO APRIL 30	10		➤ Definition: Increase marketing efforts and engage participants actively through various channels. ➤ Attribute: Increased marketing activities and participant engagement initiatives. ➤ Milestone: Increased participant registration rate.
14	Conduct safety planning and emergency response protocol. • Assess potential risks and hazards associated with the event. • Develop a safety plan that includes measures to mitigate risks and address emergencies. • Train staff and volunteers on emergency		5		➤ Definition: Develop safety plans and protocols for emergencies during the event. ➤ Attribute: Safety plans and emergency response protocol established. ➤ Milestone: Completion of safety planning.

	response procedures.				
15	Coordinate logistics and operations for race day. • Arrange for necessary equipment, such as race signage, water stations, and medical supplies. • Coordinate with vendors and suppliers to ensure timely delivery of materials. • Develop a detailed schedule for race day activities, including setup, registration, and start/finish line management.		10		➤ Definition: Organize logistics and operational aspects for the actual race day. ➤ Attribute: Detailed logistics and operations plan in place. ➤ Milestone: Completion of logistics coordination.
16	Arrange for timing systems and race result management. • Research and select appropriate timing systems for accurate race time recording. • Coordinate with timing system providers for delivery, setup, and testing of equipment. • Establish a race result management system for processing and publishing official results.		5		➤ Definition: Coordinate the acquisition and setup of timing systems to accurately record participants' race times and establish a process for managing and publishing the official race results. ➤ Attribute: Timely coordination with timing system providers. ➤ Milestone: Successful installation and testing of the timing systems.
17	Conduct pre-race events and activities to engage the community. • Organize a pre-race expo or fair for race packet pickup and engagement with sponsors. • Plan and schedule community outreach events like training runs and workshops. • Coordinate volunteer-led activities such as	MAY 1 TO MAY 31	3		➤ Definition: Organize engaging events and activities before the race to involve and connect with the local community, promote the event, and enhance participant experience. ➤ Attribute: Event planning and community engagement. ➤ Milestone: Successful execution of pre-race events with positive community feedback.

	fun runs and meet-and-greets with elite runners.				
18	Finalize participant logistics, including bib distribution and race packet preparation. • Develop a process for assigning bib numbers to registered participants. • Coordinate printing or production of race bibs and packets. • Organize the distribution of bibs and packets through mail or designated pickup locations.		7		➤ Definition: Ensure smooth logistics for participants by finalizing the process of assigning bib numbers, coordinating the production of race bibs and packets, and arranging their efficient distribution. ➤ Attribute: Efficient coordination of participant logistics. ➤ Milestone: Completion of bib distribution and race packet preparation.
19	Conduct final site visits and coordinate race day setup. • Conduct site visits to assess necessary preparations or modifications at the race venue. • Obtain permits and approvals from local authorities, venue owners, and stakeholders. • Develop a detailed site plan and coordinate logistics for race day setup.		10		➤ Definition: Visit the race venue to assess any necessary preparations, coordinate logistics, and ensure everything is ready for a seamless race day experience. ➤ Attribute: Thorough site visit and coordination. ➤ Milestone: Successful completion of race day setup and readiness of the race venue.
20	Ensure financial management and track income and expenses. • Create a budget outlining expected income and expenses for the event. • Establish a system for tracking financial transactions, including participant fees and sponsorships. • Regularly reconcile financial records and generate financial reports for monitoring		11		➤ Definition: Implement effective financial management practices to track and manage income and expenses associated with the event, ensuring financial stability and transparency. ➤ Attribute: Accurate financial tracking and management. ➤ Milestone: Completion of financial reports and reconciliation, demonstrating financial stability.



Human Resources:

1. Project Manager is responsible for all 20 tasks throughout the project.
2. GWMC officials: The people from this organization are involved and responsible for the tasks which are numbered 2,5,6,10,14,15, 18, 19.
- 3.GFPDSS Officials: The people from this organization are involved and responsible for the tasks which are numbered 7,9,11,12, 13,20.
4. Volunteers: The volunteers (both boys and girls) are involved and responsible for the tasks which are numbered 4,8,17,19.

PROJECT BUDGET

Resources Budget						
Resources		Expense Type Operating /Capital	Amount/month \$	Staff Time (Estimated)	Total Cost	Notes
Human Resources	Sai Teja (Project Manager)	Operating	1000	5 months	5000	Monthly salary for the Manager
	GWMC Officials	Operating	N/A	3 months	3300	All activities taken care by this organization according to the project structure and project schedule which includes the necessary support from the government, permissions from local authorities etc.(Excluded from total to avoid duplication as the sum is a cumulative part of all GWMC inclusions)
	GFPDSS Officials	Operating	N/A	2 months	1350	All activities taken care by this organization according to the project structure and project schedule which includes the website creation, participant registration, marketing etc.(Excluded from total to avoid duplication as the sum is a cumulative part of all GFPDSS inclusions)
	Volunteers	Operating	N/A	1 month	1000	Each volunteer gets a small food and drink coupon code on the event day
Equipment and Tools	Computer/laptop	N/A	N/A	N/A	0	Already owned
	Project management software	Operating	50	N/A	250	Monthly subscription for Microsoft 360
	Communication tools	N/A	N/A	N/A	0	Free
	Collaboration tools	N/A	N/A	N/A	0	Free
Facilities	Personal workspace	N/A	N/A	N/A	0	Already available
Materials and Supplies	Office supplies	Operating	100	N/A	500	Paper, pens, folders
	Software licenses	Operating	200	N/A	1000	Licensing fees
Information and Documentation	Project plans	N/A	N/A	N/A	0	Already created
	Requirements documents	N/A	N/A	N/A	0	Already created

	Design documents	N/A	N/A	N/A	0	Already created
	User manuals	N/A	N/A	N/A	0	Already created
	Reports and templates	N/A	N/A	N/A	0	Already created
Time and Schedule	Project schedule or timeline	N/A	N/A	N/A	0	Already created
	Task management software or tools	Operating	20	N/A	100	Trello Bard
Communication and Stakeholder Engagement	Communication plans	N/A	N/A	N/A	0	Already created

Schedule Activities

	1. Define project scope and objectives	N/A	N/A	N/A	0	No additional expense
	2. Conduct initial research on potential routes	Operating	N/A	N/A	200	expense is a part of GWMC officials
	3. Develop project plan and timeline	N/A	N/A	N/A	0	No additional expense
	4. Start volunteer recruitment efforts	N/A	N/A	N/A	0	No additional expense
	5. Finalize project plan and obtain necessary approvals	operating	N/A	N/A	100	expense is a part of GWMC officials(application forms, fee, paid approvals)
	6. Complete route selection and obtain permits	Operating	N/A	N/A	500	Permit fees(expense is a part of GWMC officials)
	7. Launch participant registration	Operating	N/A	N/A	100	Marketing expenses, website maintenance, hosting the website(expense is a part of GFPDSS officials)
	8. Continue volunteer recruitment	N/A	N/A	N/A	0	No additional expense


	9. Execute marketing strategies	Operating	N/A	N/A	500	Paid Promotions, advertising ads (expense is a part of GFPDSS officials)
	10. Coordinate with local authorities for road closures and traffic management	Operating	N/A	N/A	200	expense is a part of GWMC officials(Paid approvals for all the road activities)
	11. Continue participant registration	N/A	N/A	N/A	0	expense is a part of GFPDSS officials
	12. Finalize sponsorships	Capital	N/A	N/A	500	expense is a part of GFPDSS officials (conducting the auction)
	13. Intensify marketing efforts	Operating	N/A	N/A	0	Marketing expenses encourage more participant registration (expense is a part of GFPDSS officials)
	14. Safety planning and protocols	Operating	N/A	N/A	50	expense is a part of GWMC officials (first aid, drinking water, sun protection, emergency services)
	15. Coordinate logistics and operations	Operating	N/A	N/A	400	expense is a part of GWMC officials (audience seating, chairs, electronic equipment)
	16. Timing systems and race results	Operating	N/A	N/A	100	Timing systems delivery and setup from the providers and electricians.
	17. Pre-race events and activities	Operating	N/A	N/A	200	Event expenses for decorations and transportation of goods and services
	18. Participant logistics	Operating	N/A	N/A	1500	Logistics expenses(expense is a part of GWMC officials)
	19. Site visits and race day setup	Operating	N/A	N/A	350	Last minute hurdles, change of plan at some areas (expense is a part of GWMC officials)
	20. Financial management	Operating	N/A	N/A	250	To track all the income and expenditure with a dedicated software tool(expense is a part of GFPDSS officials)
	21. Labor Day Half Marathon Event	Operating	N/A	N/A	10000	Event expenses inclusive of post-event celebrations and some food and drinks, all other external factors on the day of the event.
TOTAL \$					22800	

Narrative Description of Expenses:

1. Project Manager Expenses: The manager is responsible for the complete organizing of the project. He needs to take care of each and every task as per the work breakdown structure. Hence, he needs to be a paid employee to work on a monthly basis. So the charge for him is \$5000.
2. GWMC Officials: This is a government organization responsible to give the necessary permissions for the event, traffic management, permits, road closures, logistics etc, discussed in the above table. Each expense named as a part of GWMC expense is a part of it.
3. GFPDSS Officials: This is a welfare body that is responsible for marketing and promotion. It also takes care about the website, participant registration, financial tracking, advertising, etc and all other expenses mentioned in the table.
4. Volunteers: They are a big team of people, who are like the pillars of the event. Their food and beverage expenses are taken care of.
5. Project Management software: All the paperwork of the project and other documents are managed with a paid version of the software.
6. Office Supplies: All the necessary office equipment (stationery items, desks, tools) is provided at a minimal cost.
7. Software Licenses: Microsoft 360 paid version.
8. Task Management Software: Trello Board
9. Timing Systems and Race Results: All the necessary electronic equipment needs to be fixed by the electricians and need to be tested perfectly.
10. Pre-Race Events and Activities: All the activities which are a part of race event are to be re-harsed before the day and logistics need to be perfect for the next day.

11. Labour Day Half Marathon Event: Emergency services, food and beverages on the event day, participant gifts on the event day, audience engagement, roll out activities.

EMPATHY MAP

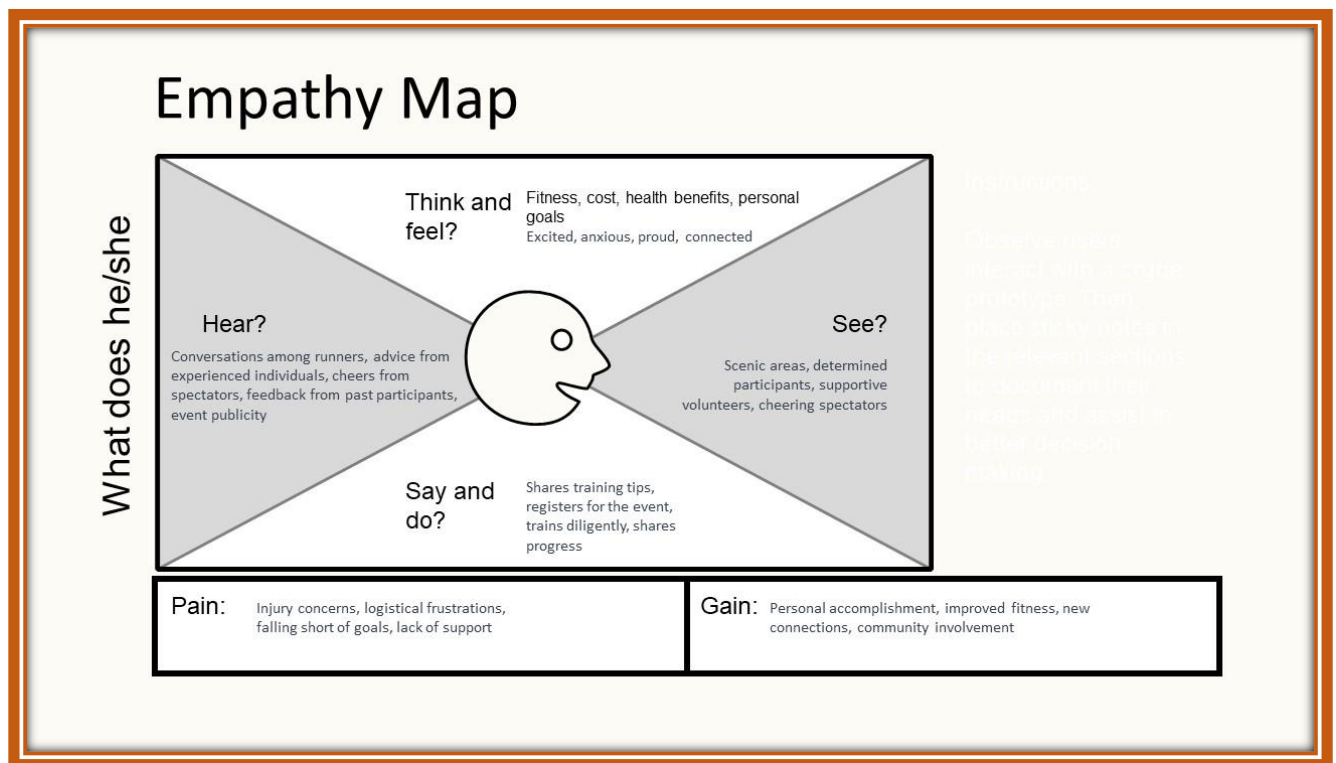

PROJECT CLOSURE

Checklist

S N O	TASK	Status of Completion	Notes
1	Define project scope and objectives, planning the project	Completed on Jan 10	Project paperwork is completely finished and proceeds for implementation.
2	Conduct initial research on potential routes and Plan it.	Completed on Jan 17	A decent road map was identified along with the GWMC officials
3	Begin developing the project plan and timeline.	Completed on Jan 22	Implementation is in phase and timelines are added.
4	Start volunteer recruitment efforts.	Completed on Jan 31	A group of volunteers are done with their registration.
5	Finalize project plan and obtain necessary approvals.	Completed on Feb 6	All approvals are cleared.
6	Complete route selection and obtain permits.	Completed on Feb 18	All permission from the city officials are taken.
7	Launch participant registration system and marketing campaigns.	Completed on Feb 25	Website development is done for registration.

8	Continue volunteer recruitment and training.	Ongoing	Training of volunteers is completed.
9	Execute marketing and promotion strategies.	Completed on March 9	Banners, flyers, promoting materials are used for marketing.
10	Coordinate with local authorities for road closures and traffic management.	Completed on March 19	There are no traffic constraints in the area.
11	Continue participant registration and communication.	Ongoing	All participant issues are sorted.
12	Finalize sponsorships and fundraising initiatives.	Completed on March 31	Identified the sponsors and received the funds from them.
13	Intensify marketing efforts and participant engagement.	Completed on April 10	All efforts are made to increase the participants by promotions.
14	Conduct safety planning and emergency response protocol.	Completed on April 15	Disaster response force help is taken and permissions are approved.
15	Coordinate logistics and operations for race day.	Completed on April 25	All logistical operations are taken care of by the volunteers.
16	Arrange for timing systems and race result management.	Completed on April 30	Scoreboards, event display boards, and necessary electronic equipment is tested and working.
17	Conduct pre-race events and activities to engage the community.	Completed on May 3	A rehearsal is made to understand the problems.

18	Finalize participant logistics, including bib distribution and race packet preparation.	Completed on May 10	Each participant received the instructions regarding the bib distribution.
19	Conduct final site visits and coordinate race day setup.	Pending, will be completed by May 20	All places surrounding the race track have to be checked thoroughly by all the officials.
20	Ensure financial management and track income and expenses.	Ongoing, will start on May 21 st and will be completed by May 30	All expenses on race day should be calculated according to the budget plan.

The estimation time of Incomplete tasks:

1. The final visits and the coordination of the race day setup is still pending. This will be completed by May 20. It takes total 10 days to complete all the logistic setup and obtain all the final pending approvals from the local authorities.
2. The financial budget management is always a thing that should be tracked on a daily basis until the event takes place. Once the logistics setup is done, all the financial documents will be cleared by May 30.

LESSONS LEARNED

I realized personally that every event in life can only be properly appreciated when I immerse myself in it. At first, event planning was straightforward enough, requiring only a few encounters with people who had money to spare. However, as I became part in the process, my perspective shifted substantially. When I placed my strategy on paper, such as incorporating GWMC and GDPDSS authorities in our event, I understood it wasn't just a question of pen and paper any longer. Everyone engaged, from the receptionist to the MLA, became a factor. I

believe it has become my obligation to communicate effectively and reach out to everyone. I also discovered the hard way that sharing and cooperating with everyone is essential. There would be little clarity about the occurrence if adequate communication was not maintained. The process of thinking about, arranging, and executing an event proved to be rather difficult. But with each event we produced, I learned something new, and with time, I got more skilled at event planning.

What motivated me to proceed forward?

A number of factors contributed to the decision to have a half-day marathon event. First and foremost, my desire to promote a healthy lifestyle and exercise in the community motivated me to take on this challenge. I was certain that such an event might have a good influence on people's lives.

Second, the opportunity to provide participants and the community as a whole with a meaningful and unforgettable experience was a motivating motivation. I saw individuals getting together, challenging themselves, and achieving personal objectives in the name of a noble cause.

Furthermore, the success of earlier events or initiatives may have influenced my decision to embark on this current effort. Positive comments and a sense of success from previous marathons most likely spurred the decision to arrange a half-day marathon.

Finally, the notion of venturing into event planning and community participation as a lone wolf seemed enticing. Despite the fact that I didn't have a team to share my hobbies and

camaraderie with, the urge to create something spectacular and contribute to the marathon event spurred my energy. Taking on all of the obligations alone allowed me to really immerse myself in the project, push myself, and fully explore my talents. While it was different from working as a team, tackling the event alone allowed me to uncover new skills and improve both personally and professionally.

What didn't go as per the plan on the paper?

As a one-person team, I must acknowledge that certain parts did not go as well as intended, one of which was the project's itinerary. In retrospect, the route plan should have been more intelligently constructed, adding notable landmarks and tourist sites along the way. Although the route was charming on its own, including these components would have improved the entire experience for participants.

Another part that did not go as planned was the food truck planning. Managing things on my own made it difficult to carry out this phase efficiently. While I intended to present attendees with a range of gastronomic alternatives, the organization and logistics with the food truck vendors did not go as anticipated. Nonetheless, these problems taught me vital event planning lessons and pushed me to enhance my organizing abilities in the future. As a part of a solitary team, I've learned to adapt and overcome challenges, and I'm committed to improving the event experience for the next chance.

Things I would like to take into consideration.

1. **Effective Planning:** With limited resources and labor, careful planning becomes even more important. I will devote significant effort to developing a precise project itinerary that includes critical milestones, deadlines, and contingencies.

2. Streamlined Route Map: In order to provide participants the greatest experience possible, I'll carefully select the route map, including iconic sites, tourist attractions, and intriguing landmarks. A well-planned route will increase the event's value and attract more attendees.
3. Logistics and execution will be of particular importance to me as a lone organizer. This will entail pre-event communication with suppliers, partners, and volunteers (if applicable) to guarantee seamless event operations.
4. Food and refreshments: Having learned from prior issues, I'll tackle food truck organizing with a more structured and detailed method. This will entail early contact with vendors, clearly establishing expectations, and having a backup plan in place in case of an emergency.
5. Participant involvement: I'll look for methods to include people before, during, and after the event to foster a feeling of community and involvement. Using social media, interactive tasks, and feedback systems can make participants feel more connected.
6. Participants' safety and security will be a key focus. I'll identify possible dangers, develop an emergency response plan, and convey safety precautions to all parties involved.
7. Personal Well-Being: Organizing an event by myself might be difficult, so I'll keep my well-being in mind throughout the process. Setting aside time for relaxation, self-care, and asking aid from friends or family will assist in maintaining a good balance.
8. Budget Management: Given the event's limited resources, I'll maintain a tight check on budget allocation, looking for cost-effective options without sacrificing event quality.

9. Flexibility and Adaptability: As a one-person team, I'll rely on my flexibility and adaptability to deal with any unanticipated issues that emerge throughout event preparation and execution.
10. Learning and Development: Each event will provide opportunities for learning and development. I'll make notes on what went well and what didn't in order to better future events.

People we would/wouldn't include

1. Participants: The event is open to everyone who is interested in the event's aim and goals. Participants from various backgrounds and degrees of competence can provide new views and improve the event experience.
2. Volunteers: If you are a solo organizer, having a team of devoted volunteers may be really beneficial. Volunteers may help with on-site logistics, participant engagement, and numerous event activities, reducing burden and improving event mood.
3. Sponsors/Partners: Working with sponsors or partners can give the event with additional support, resources, and financing. Seeking collaborations with businesses or groups that share the event's subject can be advantageous to both parties.
4. Local Authorities: In some cases, engaging local authorities, such as city officials or police enforcement, may be required for permits, security, and regulatory compliance. Their assistance can help make the event go smoothly and successfully.
5. Keynote Speakers/Influencers: Depending on the nature of the event, adding keynote speakers or influencers might enhance credibility and attract additional people. Their knowledge or popularity might increase the event's value and visibility.

6. Exhibitors/Vendors: Including exhibitors or vendors connected to the event's subject might enhance participants' experiences by delivering valued items or services.
7. Media/Journalists: Inviting media representatives or journalists to the event may assist create exposure and media coverage, expanding its reach and influence.

On the other hand, there might be people or groups that you wouldn't include:

8. Direct rivals should be avoided since they may generate conflicts of interest or dilute the event's emphasis.
9. Individuals having a history of disruptive conduct or who may not connect with the event's beliefs should be carefully assessed in order to ensure a good and harmonious environment.
10. Overwhelming Number of Participants: Managing an extremely high number of participants may become overwhelming as a one-person team. Setting an appropriate restriction on the number of participants may be required.

Would I even take on this project?

I would absolutely accept this project since working as a one-person team is a tough yet fascinating opportunity. With a great interest in event planning and community involvement, I want to meticulously organize the itinerary, simplify the route map, and successfully handle logistics. While there may be challenges, I am committed to producing a memorable event while also embracing the learning and growth that it entails.

LIST OF SPONSORS:

In Association with:

1. GWMC- Government of Telangana
2. GFPDSS- Charitable organization in Warangal
3. Make In India

Sponsored by:

1. Makers of Milkshakes
2. Namibar Builders
3. Zeiss

Supporting Organizers:

1. Marwah Studios
2. Maa
3. ICMEI
